

VCL Production

Job Cards · Customer Specs · PPC

The Frappe / ERPNext app that runs the floor — customer product specifications, four job-card types, the carton calculation pipeline, and the PPC daily planning + reporting layer.

PROJECT ID	SPONSOR	PHASE
VCL-DEV-PROD-001	Tanuj Haria	Phase 7 — Carton + Traveller
REPO	WORKSPACE	THIS REPORT
github.com/tjharia93/vcl-production	/app/vcl-production · /app/ppc	28 May 2026

Where we are today

Status as at 21:30 EAT, 28 May 2026 against the live site.

CPS RECORDS

253

customer product specifications

JOB CARDS LIVE

110

Carton 19 · Label 56 · CP 35

DOCTYPES

22

across 3 modules

PPC REPORTS

10

live for the planning desk

One sentence: The Production Log app is in active build — Job-Card-Tracking is the foundation (Customer Product Spec + four submittable Job Cards + traveller / resource child tables) and the PPC layer (Daily Plan, Production Actual + ten reports) sits on top. The current focus is the Carton job traveller PDF and the per-line stage ladder; the Computer-Paper, Label, and ETR job cards are stable.

What's running on the live site

WHAT	STATE	HEALTH
Customer Product Specification	Single master doctype with 253 live records. Auto-toggles GSM / colour / packing sections by pLy and product_type. Used by every job card.	• LIVE
Job Card Carton	19 records. Submittable. RSC / 1-flap / 2-flap / 3-flap / Tray geometry → board sizes + weight pipeline. Print format is a 4-6 page traveller (PDF generator = Chrome).	• LIVE
Job Card Label	56 records. Submittable. Spec snapshot auto-populates from CPS. Slack notification on submit via n8n.	• LIVE
Job Card Computer Paper	35 records. Submittable. Colour-of-Parts child table for per-part GSM / colour rows.	• LIVE
Job Card ETR	Live. Reel-to-reel printing for thermal / receipt rolls. Print format separate from the other three (different schema: status / delivery_date).	• LIVE

WHAT	STATE	HEALTH
PPC Daily Plan + Production Actual	Daily-plan and same-day-actual doctypes with item child tables. Feeds 10 query reports (Open Job Pool, Closed Jobs, Waste, Downtime, Carry-Forward Pending, etc.).	• SOFT LIVE
Job Traveller Run + Resource Consumption	Child tables on all 4 job cards (deployed 19-20 May). Capture stage / operator / quantity / time + planned-vs-actual material variance. Render in the print format Jinja loops.	• LIVE
Workstation product-line tag ladder	14 workstation types, 33+ tag rows numbered by process_number per product line (R2R, Trading, GSE, Mono Boxes, Self-Adhesive Label, Sheet-to-Sheet, Carton, Exercise Books). Codified in patch v7_4.	• LIVE
17:00 EOD Gemba report → Telegram	Frappe scheduler → gemba.py → n8n webhook (vclGembaTelegram001) → Telegram sendDocument. n8n holds the bot token (Frappe Cloud doesn't).	• NEEDS SITE_CONFIG



What's in the app

One Frappe app (production_log), three modules, 22 doctypes, 10 reports, 44 patches deployed since v3.

MODULE 01

Job Card Tracking

16 DOCTYPES

Customer Product
Specification · Job Card Carton
/ Computer Paper / ETR / Label
· Job Traveller Run · Job
Resource Consumption · Dies ·
Dies Order · Colour of Parts ·
Pantone Colour · Spot Colour ·
Carton Job Type UPS · ETR
Plate Detail · ETR Print Reel
Output

MODULE 02

PPC

4 DOCTYPES · 10 REPORTS

PPC Daily Plan + Item · PPC
Production Actual + Item ·
Open Job Pool · Daily Plan
Report · Production Actual
Summary · Completed Awaiting
Closure · Closed Jobs ·
Packing Pending · On Hold ·
Waste · Downtime · Carry-
Forward Pending ·
Rejection/QC

MODULE 03

Production Log

3 DOCTYPES

Production Entry · Production
Schedule Line · Workstation
Product Line Tag

This module is the "execution layer" leftovers – most of it was removed in the v3 reset; what survives is the stage ladder + per-line route tagging.

The carton job pipeline

One Customer Product Spec drives one Job Card which renders one multi-page traveller PDF. Traveller runs and resource consumption capture the floor reality. Daily Plan rolls multiple Job Cards into the day's schedule.

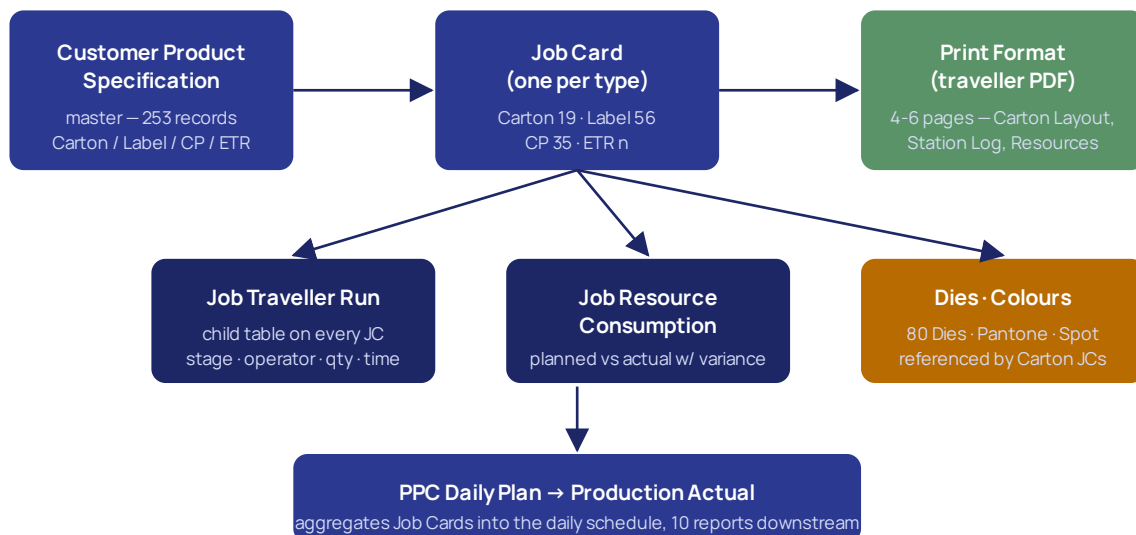


Figure 1. The CPS → Job Card → Print Format pipeline, with Traveller / Resource child tables feeding the PPC layer.

The carton calculation chain (the hard bit)

1. **Ply rules** — CPS fields toggle on ply (3 → layers 1-3, 5 → 1-5, SFK → 1-2) and on product_type.
2. **SFK UI** — the special-board UI for SFK ply types.
3. **Flap auto-calc** — Tray, 1-Flap, 2-Flap, 3-Flap, RSC geometry formulas in `vcl_calc_board_sizes_serial`.
4. **Board sizes** — planned + actual width × length, both planned by the spec and actual measured on-floor.
5. **Weight calc** — derived from board sizes + GSM per layer.
6. **Print format** — 4-6 pages: Job Card, Carton Layout (full-width die-cut SVG), Station Log (Jinja loop over Traveller Runs), Resources (planned vs actual + variance).



What you see at /app/vcl-production

Captured today against `https://vimitconverters.frappe.cloud` via Playwright with API-token auth.

The screenshot displays the VCL Production workspace interface. The top header shows 'VCLProduction · workspace' on the left and '/app/vcl-production' on the right. The sidebar on the left contains a search bar, a notification bell, and a list of navigation links: Home, Customer Product Speci..., Dies List, New Computer Paper Jo..., Computer Paper Job Ca..., New Label Job Card, Label Job Cards, New Carton Job Card, and Carton Job Cards. The main content area is titled 'VCL Production' and features three sections: 'Customer Specifications' with buttons for 'Customer Pr...' (253) and 'Dies List' (80); 'Job Card Tracking' with buttons for 'New Computer Pa...' (35), 'Computer Pap...' (35), 'New Label Job Card', 'Label Job Car...' (56), 'New Carton Job C...', and 'Carton Job Ca...' (19); and 'Daily Planning'. The bottom of the sidebar shows a user profile for Tanuj Haria with the email tanuj.haria@vimit.com.

Top-level workspace. Customer Specifications (253 CPS + 80 Dies) + Job Card Tracking (Carton 19, Label 56, Computer Paper 35) + Daily Planning shortcuts. Sidebar pins the same links for one-click access from anywhere.

P PPC
Production Log

/ PPC

Q Search Ctrl+K

Notification

Home

PPC Computer Paper Bo...

New Daily Plan

Daily Plans

Production Actuals

Open Job Pool

Daily Plan Report

Production Actual Summ...

Completed Awaiting Clo...

Closed Jobs

Packing Pending

On Hold

Waste

Downtime

Rejection / QC

Carry Forward Pending

TH Tanuj Haria
tanuj.haria@vimit.com

PPC Computer Paper

PPC Computer Pa... ↗

New Daily Plan ↗ 1

Daily Plans ↗ 1

Production Act... ↗ 5

Reports

Open Job Pool ↗

Daily Plan Report ↗

Production Actual ... ↗

Completed Awaitin... ↗

Closed Jobs ↗

Packing Pending ↗

On Hold ↗

Waste ↗

Downtime ↗

Rejection / QC ↗

Carry Forward Pen... ↗

The PPC planning desk — Daily Plan + Production Actual at the top, then a 10-card report grid: Open Job Pool, Daily Plan Report, Production Actual Summary, Completed Awaiting Closure, Closed Jobs, Packing Pending, On Hold, Waste, Downtime, Rejection/QC, Carry-Forward Pending. Each is a saved query report.

Lists you live in

Customer Product Specification list

/app/customer-product-specification

V VCL Production

Search Ctrl+K

Notification

Home

Customer Product Speci...

Dies List

New Computer Paper Jo...

Computer Paper Job Ca...

New Label Job Card

Label Job Cards

New Carton Job Card

Carton Job Cards

TH Tanuj Haria
tanuj.haria@vimit.com

/ VCL Production / Customer Product Specification

List View Saved Filters

+ Add Customer Product Specification

ID ≈ Product Type Status Specification ≈ Customer

Filter x Last Updated On

ID	Status	Product Type	Specification Name	Customer	20 of 253
☐ CPT-SPEC-0003	Submitted	Computer Paper	MIKELINE DETERGENT (INVOICE) - HEADQUARTER - R...	JOHN MBURI	2 d 0 0
☐ CPT-SPEC-0003	Submitted	Computer Paper	MIKELINE DETERGENT (INVOICE) - CBD NAIROBI	JOHN MBURI	2 d 0 0
☐ CPT-SPEC-0003	Cancelled	Computer Paper	MIKELINE DETERGENT (INVOICE) - CBD NAIROBI	JOHN MBURI	2 d 0 0
☐ CTN-SPEC-0001	Submitted	Carton	500ML CARTON	Farmstream S	3 d 0 0
☐ CTN-SPEC-0001	Cancelled	Carton	500ML CARTON	Farmstream S	3 d 0 0
☐ CTN-SPEC-0001	Submitted	Carton	250ML CARTON	Farmstream S	5 d 0 0
☐ CPT-SPEC-0003	Submitted	Computer Paper	RAJ CHEM POLYMER LTD - INVOICE	RAJCHEM PC	6 d 0 0
☐ ETR-SPEC-0000	Submitted	ETR (Reel to Reel ...)	TIRYO GENERAL MERCHANDISE - ETR	TIRYO GENE	6 d 0 0
☐ LBL-SPEC-0003E	Submitted	Label	Label 198 - PP1011 BLK Punnet	THERMOPAK	6 d 0 0
☐ LBL-SPEC-00157	Submitted	Label	DFC1 LABEL	ROK INDUST	6 d 0 0
☐ LBL-SPEC-0014C	Submitted	Label	SC3	ROK INDUST	6 d 0 0
☐ CPT-SPEC-0003	Submitted	Computer Paper	EAST AFRICAN CABLES - INVOICE	EAST AFRICA	6 d 0 0
☐ CPT-SPEC-0003	Submitted	Computer Paper	EAST AFRICAN CABLES - LPO	EAST AFRICA	6 d 0 0
☐ CPT-SPEC-0003	Cancelled	Computer Paper	EAST AFRICAN CABLES - LPO	EAST AFRICA	6 d 0 0
☐ CPT-SPEC-0003	Cancelled	Computer Paper	EAST AFRICAN CABLES - INVOICE	EAST AFRICA	6 d 0 0
☐ LBL-SPEC-00189	Submitted	Label	Green Spoon - 1 Litre - Mango Juice	GREENSPOO	6 d 0 0
☐ LBL-SPEC-00188	Submitted	Label	Green Spoon - 1 Litre - Tropical Bliss	GREENSPOO	6 d 0 0

20 100 500 2500 Load More

Single doctype hosting all four product types. 253 records – CPT- (Computer Paper), CTN- (Carton), ETR-, LBL-SPEC- prefixes show the type. Status chip (Submitted / Cancelled / Draft) drives downstream Job Card creation. List view pinned to "Last Updated On".

V

VCL Production

▼

Q Search

Ctrl+K

🔔 Notification

Home

Customer Product Speci...

Dies List

New Computer Paper Jo...

Computer Paper Job Ca...

New Label Job Card

Label Job Cards

New Carton Job Card

Carton Job Cards

TH

Tanuj Haria

tanuj.haria@vimit.com

/ VCL Production / Job Card Carton

List View

Saved Filters

⌂

⋮

+ Add Job Card Carton

ID

≈

Status

Customer Name

Customer Product

Job Status

Filter

×

Last Updated On

▼

ID	Status	Customer Name	Print Type	Job Status	19 of 19	♥
☐ JC-CORR-2026-0055-1	Draft	Farmstream Suppliers	• Plain	• Open	3 d	0 • ♥
☐ JC-CORR-2026-0055	Cancelled	Farmstream Suppliers	• Plain	• Open	3 d	0 • ♥
☐ JC-CORR-2026-0052-1	Submitted	VIMIT CONVERTERS LIMITED	• Plain	• In Progress	3 d	0 • ♥
☐ JC-CORR-2026-0053	Submitted	GOSHRANI PRINTERS LIMITED	• Plain	• In Progress	3 d	0 • ♥
☐ JC-CORR-2026-0054	Submitted	Farmstream Suppliers	• Plain	• Open	3 d	0 • ♥
☐ JC-CORR-2026-0052	Cancelled	VIMIT CONVERTERS LIMITED	• Plain	• Open	1 w	0 • ♥
☐ JC-CORR-2026-0045	Submitted	EAST WEST AFRICA LTD	• Printed	• Completed	1 w	1 • ♥
☐ JC-CORR-2026-0051	Submitted	DOULCEPACK PACKAGING SUPPLIES	• Plain	• Open	1 w	0 • ♥
☐ JC-CORR-2026-0050	Submitted	VISTA PACKAGING LIMITED	• Plain	• Open	2 w	0 • ♥
☐ JC-CORR-2026-0049	Submitted	BYLAB EAST AFRICA LTD	• Printed	• Open	3 w	0 • ♥
☐ JC-CORR-2026-0048	Submitted	BYLAB EAST AFRICA LTD	• Printed	• Open	3 w	0 • ♥
☐ JC-CORR-2026-0047-1	Submitted	BYLAB EAST AFRICA LTD	• Printed	• Open	3 w	0 • ♥
☐ JC-CORR-2026-0047	Cancelled	BYLAB EAST AFRICA LTD	• Printed	• Open	3 w	0 • ♥
☐ JC-CORR-2026-0046	Submitted	BYLAB EAST AFRICA LTD	• Printed	• Open	3 w	0 • ♥
☐ JC-CORR-2026-0044	Submitted	AMBROSAB ENTERPRISES LTD	• Plain	• Open	1 M	0 • ♥
☐ JC-CORR-2026-0036-1	Submitted	VIMIT CONVERTERS LIMITED	• Printed	• Open	1 M	0 • ♥
☐ JC-CORR-2026-0036	Cancelled	VIMIT CONVERTERS LIMITED	• Printed	• Open	1 M	0 • ♥

20

100

500

2500

19 carton job cards live. ID format JC-CORR-YYYY-NNNN. Columns: Print Type (Plain / Printed) + Job Status (Open / In Progress / Completed / Cancelled). The traveller PDF renders from this doctype.



The 17:00 Gemba flow

The end-of-day Gemba report is a per-job-card-type summary (closed, in-progress, on-hold, blocked) auto-generated at 17:00 EAT and pushed to Tanuj on Telegram. The Frappe Cloud site doesn't hold the Telegram bot token — n8n does — so the flow is intentionally split.



Figure 2. The Gemba report path. Frappe builds the PDF, n8n owns the credentials and the multipart upload.

Implementation details

- **Scheduler:** 17:00 EAT entry in `production_log/hooks.py` calling `generate_eod_report`.
- **Per-doctype profile** (`JCL_PROFILE`): different job-card schemas (e.g. ETR uses `status + delivery_date`; Carton/Label use `job_status`) get aliased in the SQL so one report template covers all four.
- **Webhook:** `https://vcl-intranet.tailb2b755.ts.net/webhook/gemba-telegram` — n8n workflow `vclGembaTelegram001`.
- **Token:** stays in n8n's environment (`$env` read inside the Code node). No Frappe `site_config` secret.
- **Default chat:** 8566637123 (Tanuj). Override via `site_config` `gemba_chat_id` only if needed.

What still blocks the flow on prod

ITEM	WHY IT MATTERS
<code>site_config.telegram_bot_token</code>	Required only for the legacy direct-Telegram path — now bypassed via n8n. Keep absent or remove.
<code>site_config.gemba_channel_chat_id</code>	Optional. Defaults to Tanuj's personal chat if absent. Set if you want to push to a group instead.

What we shipped in the last 30 days

Pulled from `CHANGELOG_DAILY.md` + git log. Only the load-bearing commits — for the full daily log read the file.

-
- 19 May** **S1 + S2 deploy (build #5).** Job Traveller Run + Job Resource Consumption shipped as child doctypes; `print_type` + 5 readiness Check fields added across all four job-card types; Carton traveller print format redesigned with Jinja loops over the 8-station ladder; 14 Carton CPS records backfilled with `print_type`.
-
- 20 May** **v7_1 patch silent-failure HOTFIX.** 2 workstation types (Slotting, Bundling) + 2 workstations (Slotter 01, Bundler 01) inserted manually after the patch's `try/except` `NameError` swallowed the failure. Resolved permanently in `v7_3.finish_carton_workstations` (idempotent).
-
- 20 May** **Stage ladder + per-line route model.** 14 workstation types numbered 15-165 (resolves the 999 collision); 26 existing route tag rows + 7 new ones numbered with `process_number`. Codified in `v7_4`. The same station now has different positions in different product lines (Sheeting = step 1 of Trading, step 5 of Exercise Books).
-
- 20 May** **EOD Gemba rewired to n8n.** `gemba.py` now POSTs `{pdf_base64, filename, caption, chat_id}` to the n8n webhook; `_resolve_telegram_credentials` and `/etc/vcl/telegram.env` fallback removed. Bot token stays in n8n.
-
- 21 May** **Notebook 32 – Carton CPS review.** 5-point review from Tanuj's reMarkable: `board_type` hidden, `printing_or_plain` retired, GSM-by-ply toggles, packing section hidden for Carton, Carton Layout moved to its own page in the traveller. 16 Property Setters + `print_type` reposition codified in `v7_5.notebook_32_carton_review`.
-
- 21 May** **Print format → Chrome PDF generator.** `wkhtmltopdf` ignored per-page orientation + collapsed the `no-viewBox` SVG. Carton print format flipped to `pdf_generator = chrome` (per-format field, not site-wide). Spurious blank pages fixed; landscape NOT achievable (Frappe site-wide `pdf_page_size` overrides CSS).
-
- 22-27 May** **Carton geometry + Job Card UI cleanup.** 8 commits — full-width die-cut SVG via Jinja `viewBox` injection, Carton Layout page added (planned + actual board sizes), `board_type` fully deleted from CPS (not hidden), `allow_on_submit` on `standard_packing` + `standard_weight_per_carton` (so they're editable after submit).
-
- 28 May** **ETR print-type snapshot fix.** `etr_print_type` snapshot was blocking all Job Card ETR saves — dropped (commit `d87988f`).

What's still open

Direct from the TODO blocks in CHANGelog_DAILY.md + the patch backlog. Owner-tagged where known.

Floor / data

ITEM	WHAT IT BLOCKS	OWNER
Hamada 01 reclassification	Currently tagged Reel to Reel Printing; likely Sheet to Sheet Printing. Wrong tag puts the press in the wrong route order on every Job Card.	<i>Tanuj</i>
Sheet-to-Sheet Printing exception tag	The Corrugation and Carton Department tag on S2S Printing has no process_number (offset-printed carton exception). Decide keep / drop.	<i>Tanuj</i>
Floor: rename Slotter 01 / Bundler 01	Generic placeholders. Need actual equipment IDs after the S3 install.	<i>Floor</i>

Print format / PDF

ITEM	WHAT IT BLOCKS	OWNER
Carton Layout landscape page	Frappe forces page size from site-wide Print Settings — CSS @page orientation is overridden. True landscape only via site-wide flip (touches every print format). Carton box renders portrait, full-width upright today — adequate but not ideal.	<i>Claude / Codex</i>
Station Log overflow page	Chrome generator improved page-break behaviour but the traveller still spills to 6 pages on dense jobs. Acceptable but could be tightened with row-height + page-break-inside fences.	<i>Claude / Codex</i>

System / config

ITEM	WHAT IT BLOCKS	OWNER
EOD Gemba on prod	Code is live; n8n webhook + token are live and verified. Site config keys (telegram_bot_token, gemba_channel_chat_id) optional but recommend at minimum confirming the default chat ID.	<i>Tanuj</i>
v7_2 follow-up patch	Daily-log mentions a follow-up to clean up after v7_1's silent failure. v7_3 covers the workstation create; check if anything else lingers.	<i>Claude</i>

Bigger questions

Q1. Production-execution layer — removed in v3. Was the new traveller + resource model enough, or do we need a slim version of Daily Production Log / Production Entry back (e.g. for cumulative WIP across days)?

Q2. Carton job-card releases — the 5 readiness Check fields (plate_ready, material_in_stock, customer_hold, artwork_approved, plates_lead_time_clear) are on every job-card type but nothing gates submit on them yet. Should they gate submit, or just be informational in a Release Plan view?

Q3. Carton ply-7 / ply-9 — current GSM toggles handle 3, 5, SFK. Anything heavier needed for export packaging?

Q4. Should the PPC reports live on a dashboard (single page, side-by-side charts) instead of separate report URLs?



What comes next

This week (29-30 May)

OWNER	ACTION	BY
<i>Tanuj</i>	Confirm Hamada 01 reclassification — is it Sheet-to-Sheet or Reel-to-Reel Printing? Direct MCP fix takes 30 seconds.	29 May
<i>Tanuj</i>	Decide on the Sheet-to-Sheet Printing exception tag (keep with no process_number / drop).	29 May
<i>Tanuj</i>	Confirm site_config for the EOD Gemba flow. End-to-end smoke test from cron → reMarkable.	30 May
<i>Claude</i>	Write a v7_6 patch to drop the orphan etr_print_type column (already removed from JSON; HOTFIX commit d87988f on main).	30 May

June

OWNER	ACTION	BY
<i>Tanuj</i>	Decide on the readiness-flag gating (Q2 above). Either ship as form-level depends_on or build a Release Plan view.	3 Jun
<i>Claude / Codex</i>	Build the Release Plan dashboard if Q2 lands as "yes, build it".	7 Jun
<i>Floor</i>	Rename Slotter 01 / Bundler 01 to actual equipment IDs after S3 install.	post-S3
<i>Claude / Codex</i>	Carton Layout landscape — only if Tanuj wants to absorb the site-wide flip. Otherwise the current portrait full-width carton box stays.	tbd

Outside this app but adjacent

- **EOD reports** — the Gemba report is one. The same pattern (Frappe → n8n → Telegram/Slack) could be reused for the PPC Daily Plan summary, Open Job Pool digest, etc.
- **The VCL PMO System (sister project)** is now the home for cross-project planning — production change requests beyond a daily-log entry can go through the PMO Plans / Shifts loop. The link is already there in the workspace sidebar.

